


NOTE:
DIVERSION BUNDS SHOWN INDICATIVELY (TYP.).
INSTALL BUNDS WHERE THERE IS A LIKELYHOOD OF
RUNOFF FLOWING OFF SITE DURING THE
EARTHWORKS PHASE

DIVERSION BUNDS ARE TO BE
REINSTATED PROGRESSIVELY AT
THE TOP OF BATTER AS
EARTHWORKS LEVELS CHANGE

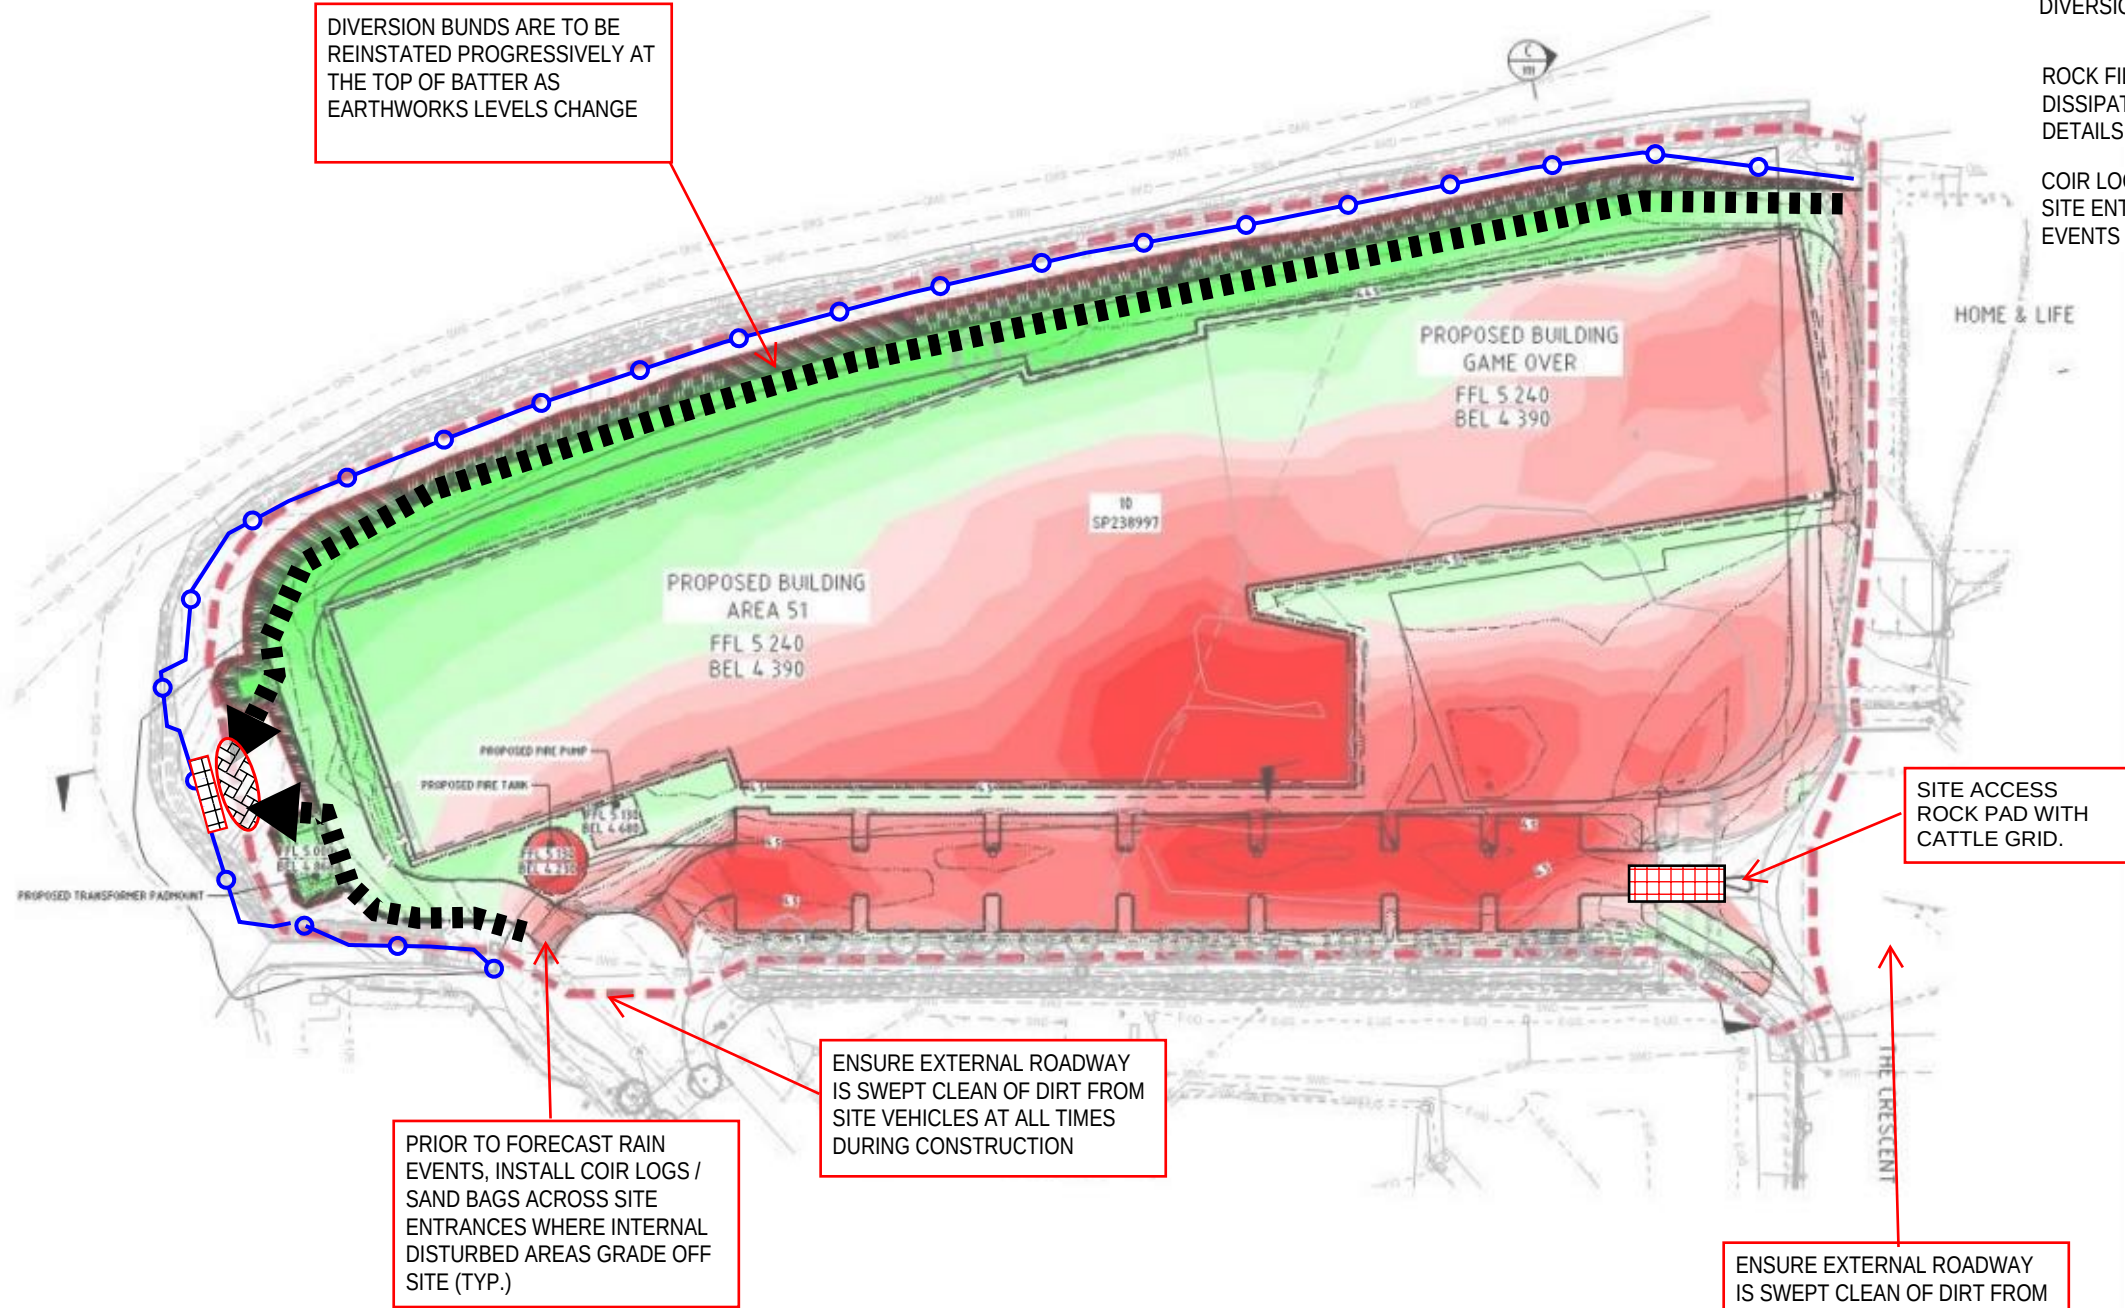

PRIOR TO FORECAST RAIN
EVENTS, INSTALL COIR LOGS /
SAND BAGS ACROSS SITE
ENTRANCES WHERE INTERNAL
DISTURBED AREAS GRADE OFF
SITE (TYP.)

ENSURE EXTERNAL ROADWAY
IS SWEEPED CLEAN OF DIRT FROM
SITE VEHICLES AT ALL TIMES
DURING CONSTRUCTION

ENSURE EXTERNAL ROADWAY
IS SWEEPED CLEAN OF DIRT FROM
SITE VEHICLES AT ALL TIMES
DURING CONSTRUCTION

SITE ACCESS
ROCK PAD WITH
CATTLE GRID.

ESC LEGEND:


- ROCK PAD CONSTRUCTION ENTRANCE TO IECA STD. DRG. EXIT-01
- SEDIMENT FENCE TO IECA STD. DRGS. SF-1 AND SF-02
- DIVERSION BUND REFER DETAIL ON DR-05
- ROCK FILTER DAM WITH ENERGY DISSIPATION APRON REFER DR-05 FOR DETAILS
- COIR LOGS / SANDBAGS INSTALLED ACROSS SITE ENTRANCES PRIOR TO FORECAST RAIN EVENTS

LEGEND

- XX.XX--- PROPOSED SURFACE CONTOURS
- XX.XX--- EXISTING SURFACE CONTOURS
- EXISTING PROPERTY BOUNDARY
- W --- EXISTING WATER MAIN
- R --- EXISTING RECYCLED WATER
- S --- EXISTING SEWER PIPE
- RM --- EXISTING SEWER PIPE RISING MAIN
- E-UG --- EXISTING ELECTRICITY (UNDERGROUND)
- SWD --- EXISTING STORMWATER DRAINAGE PIPE CL
- EXISTING STORMWATER STRUCTURES
- WORKS BOUNDARY
- SPOT LEVEL (EXISTING)
- SPOT LEVEL (DESIGN)
- PROPOSED RETAINING WALL

CUT/FILL DEPTH

DEPTH COLOUR	LOWER DEPTH	UPPER DEPTH
	-999m	-2.0m
	-2.0m	-1.5m
	-1.5m	-1.25m
	-1.25m	-1.0m
	-1.0m	-0.75m
	-0.75m	-0.5m
	-0.5m	-0.25m
	-0.25m	0.0m
	0.0m	0.25m
	0.25m	0.5m
	0.5m	0.75m
	0.75m	1.0m
	1.0m	1.25m
	1.25m	1.5m
	1.5m	2.0m
	2.0m	999m



ORIGINAL DRAWINGS PROVIDED BY NORTHROP CONSULTING ENGINEERS



CHRIS HUTTON
CPESC. 6241



89 CASLICK LANE,
BROADWATER, QLD.
PH: (MOB) 0400 643 883

APPROVED

DATE
26-05-2026



CHRIS HUTTON - CPESC No. 6241

CLIENT
NORTHROP CONSULTING ENGINEERS

PROJECT
SKYGATE PLAY

LOCATION
LOT SKG26, THE CIRCUIT, BRISBANE AIRPORT

DRAWING TITLE
EROSION AND SEDIMENT CONTROL - EARTHWORKS PHASE

JOB No.
ESC-0606

DRAWING No. / REVISION
DR-04 / a
