TABLE A: DIVERSION BUND DESIGN CALCULATIONS

Diversion Bund Label	Peak Flow Calcs						Velocity									
	INPUTS					OUTPUTS	Inputs				Outputs					
						Peak Flow	Side Slope 1	Side Slope 2	Channel Slope (m/m)	Proposed Lining	Mannings	Peak Flow	Flow Depth (m)	Flow Depth with 150mm Feeboard	Maximum Permissable Velocity (m/s)	Velocity (m/s)
	C10	Itc,y	Tc	A	F	Q	x1	x2	So		n	Q	y		Vmax	V
DB 01	0.7	97	15	2.25	0.85	0.361	2	2	0.010	Geofabric or Vital HR spray	0.0220	0.361	0.410	0.560	1.500	1.073

DIVERSION BUND CONSTRUCTION DETAILS



DIRTY WATER DIVERSION BUND DETAIL

N.T.S

CHECK DAM SPACING

GRADE (%)	SPACING INTERVAL (m) 200mm HIGH	300mm HIGH	400mm HIGH	500mm HIGH	600mm HIGH
0.5	40	60	80	100	120
1.0	20	30	40	50	60
2.0	10	15	20	25	30
3.0	6.7	10	13	17	20
4.0	5.0	7.5	10	13	15
5.0	4.0	6.0	8.0	10	12
10.0	2.0	3.0	4.0	5.0	6.0
15.0	1.3	2.0	2.7	3.3	4.0

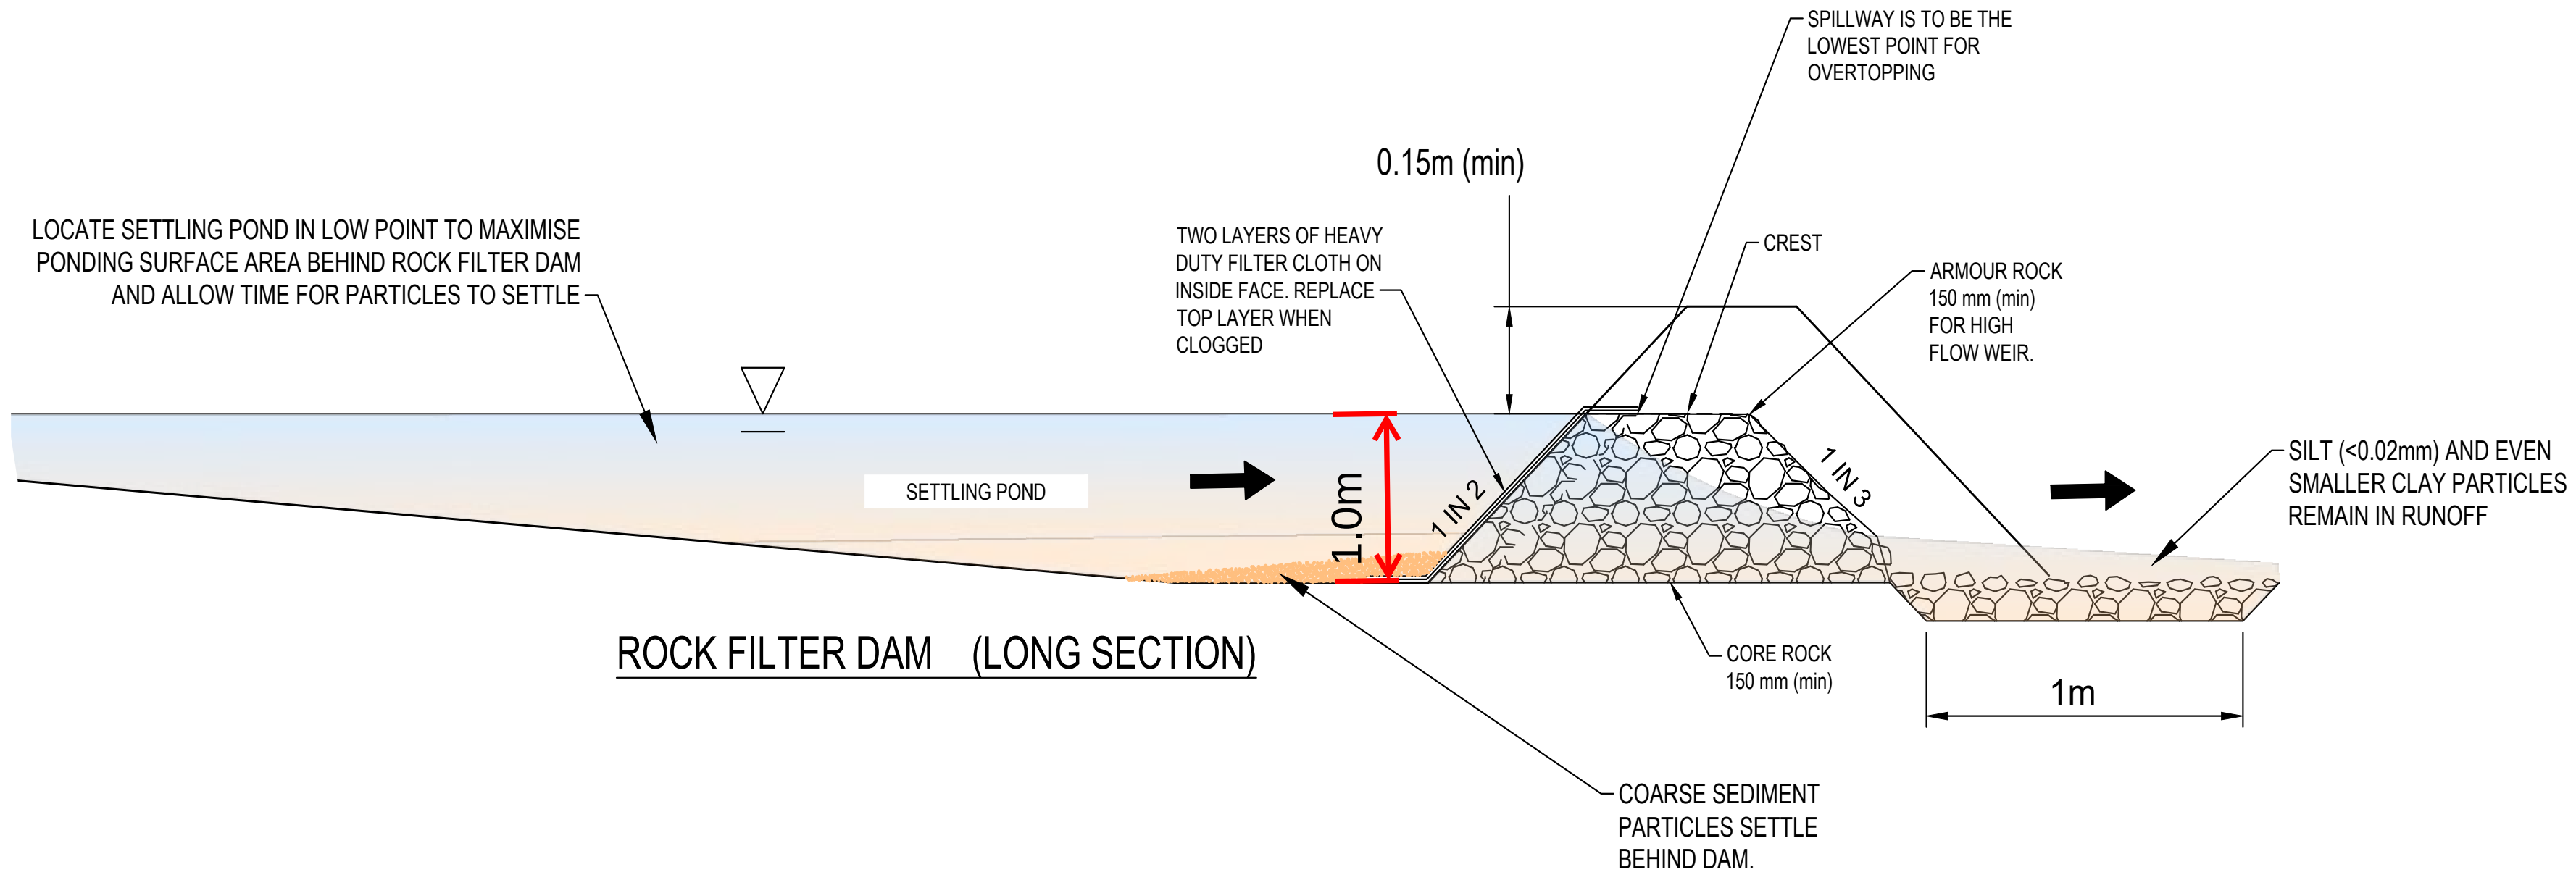

ROCK FILTER DAM (LONG SECTION)

RECOMMENDED DISCHARGE STANDARD FOR DEWATERING OPERATIONS.	
SITE CONDITIONS	DISCHARGE WATER QUALITY STANDARD
POST STORM DE-WATERING	• Turbidity – project specific correlation between turbidity and TSS to be established (use 50 NTU at start of project if no correlation) pH 6.5 TO 8.5

ROCK FILTER DAM EXAMPLE

CHRIS HUTTON
CPESC. 6241

89 CASLICK LANE, BROADWATER, QLD.
PH: (MOB) 0400 643 883

APPROVED	DATE	CLIENT	NORTHROP CONSULTING ENGINEERS	JOB No.	ESC-0606
CHRIS HUTTON - CPESC No. 6241	26-05-2026	PROJECT	SKYGATE PLAY		
		LOCATION	LOT SKG26, THE CIRCUIT, BRISBANE AIRPORT		
		DRAWING TITLE	EROSION AND SEDIMENT CONTROL - DIVERSION BUND & FILTER DAM DETAILS	DRAWING No. / REVISION	DR-05 / a

ESC Environmental Solutions
